Earthquake Safety and Emergency Response Bond Program



ESER 2010/2014 Neighborhood Fire Stations

Agenda


• Projects' Scope, Budget & Schedule Update

Presentation to SF Fire Commission

May 28, 2015



Projects' Status Map

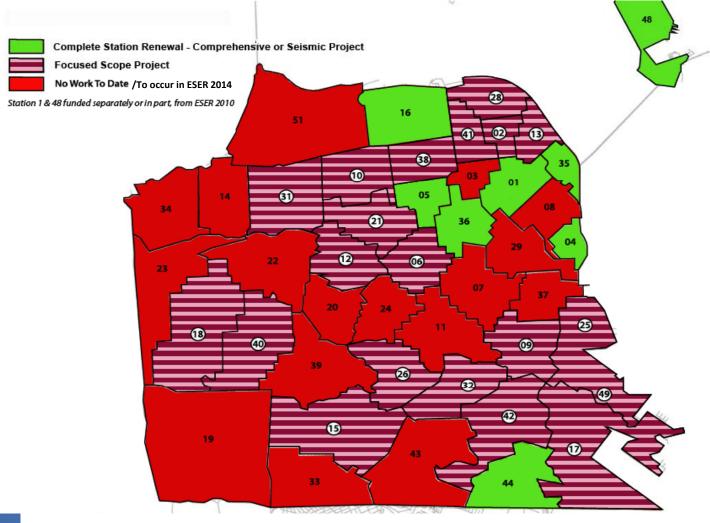



ESER 2010: Neighborhood Fire Stations
Focused Scope – Budget \$12.2 Million - 84% expended

Roofs: 15 stations completed

[2, 6, 10, 13, 15, 17, 18, 26, 28, 31, 32, 38, 40, 10, 42]

Exterior Envelope: 16 stations completed

[2, 6, 10, 13, 15, 17, 18, 26, 28, 31, 32, 38, 40, 41, 42, 49]

Emergency Generator: 4 of 5 stations completed

[6, 12, 15, 17, 21]

Shower: 8 stations completed

[15, 6, 13, 18, 40, 41, 26, 38]

Mechanical: 15 stations completed

[6, 10, 13, 15, 17, 18, 26, 28, 31, 32, 38, 40, 41, 42]

Windows: 12 stations completed

[2, 6, 17, 25, 26, 28, 31, 32, 38, 40, 41, 42]



Focused Scope



FS10 roof flashing @ mechanical unit



FS21 emergency generator



FS17 exterior envelope



FS18 mechanical



Comprehensive Scope – Budget: \$6.3 million - 100% expended

Station 36

- Completed and reactivated November 19, 2014.
- Public Works is managing the resolution of issues communicated post-occupancy with consultant architect and builder. Some issues require additional work and will result in change orders.

Station 44

 Completed and reactivated May 22, 2014



FS36 kitchen



FS44 view from Wilde Ave @ Girard St.



Seismic Scope - Budget: \$22.6 million - 13% expended

Station 5 – Western Addition

- In design development phase. Civic design review Phase II was approved in April; SFAC Visual Arts selection of Artist underway.
- Of responding firms to RFQ for CM/GC, five (5) have been pre-qualified; construction anticipated to begin Fall 2016

Station 16 – Marina / Cow Hollow

- Categorical exemption appeal was denied by Board of Supervisors in May;
 permit appeal hearing is scheduled on June 24.
- Four responding construction firms to RFQ were qualified; construction is anticipated to begin in Summer 2016

Station 35 - Fire Boats' HQ/Embarcadero & So. Beach

 Early planning expenses expended \$617K; balance of funding to be drawn from ESER 2014.





FS5 Rendering



FS16 Rendering – view from Greenwich St. FS16 Rendering – view from Pixley St.





Immediate Focused Scope - Budget \$10.7 Million - 1% expended

Additional Focused Scope - Budget TBD

Roofs: 3 stations

[3, 43, 49]

Exterior Envelope: 5 stations

[8, 23, 29, 24, 34]

Emergency Generator: 3 stations

[19, 31, 39]

Showers: 4 stations

[13, 20, 22, 34]

Mechanical: 9 stations

[7, 8, 14, 20, 22, 23, 41, 42, 49]

Windows: 9 stations

[8, 9, 19, 20, 21, 24, 29, 25, 7 training tower]

Sidewalk Repair: 4 stations

[13, 31, 20, 26]

Access Control: 41 stations



Comprehensive Scope – Budget: \$TBD million - 0% expended

Stations candidate sites TBD;

Seismic Scope - Budget: \$41.5 million - 1% expended

• Station 35 – (\$40M) Fire Boats' HQ/Embarcadero & South Beach – Preliminary Planning underway – anticipated start of construction (date)

Key Dates Chronology

- October 2012 Project at existing site/Pier 22 1/2 put on-hold pending determination of Warriors Arena project at Piers 30/32
- **April 2014** Warriors Arena project moved to Third Street
- **August 2014** Functional programming initiates
- **September 2014** Port of SF adopts Sea Level Rise Guidance Report
- January 2015 Alternative building massing studies developed
- May 2015 Preliminary cost estimates for alternative schemes
- Station 48 (\$1.5M) Treasure Island



- Completed May 2015





Questions/Discussion
